| # | Activity Name | Activity Count | Original Duration | Activity % Complete | Start | Finish |
|---|---|---|---|---|---|---|
| 1 | **MAGIC-1** | 18 | 375d | | 15-Sep-25 A | 28-Apr-27 |
| 2 | MAGIC:OoB VH & Supp : Procurement of OoB housing and supports | 1 | 60d | 20% | 15-Sep-25 A | 05-Dec-25 |
| 3 | MAGIC:OoB VH & Supp: Manufacturing | 1 | 160d | 0% | 08-Dec-25 | 07-Sep-26 |
| 4 | MAGIC:OoB VH & Supp: Factory Acceptance Test (FAT) | 1 | 0d | 0% | 08-Sep-26 | |
| 5 | MAGIC:OoB VH & Supp: FAT Report and Documentation | 1 | 5d | 0% | 08-Sep-26 | 14-Sep-26 |
| 6 | MAGIC:OoB VH & Supp: FAT-closure of open points and approval | 1 | 10d | 0% | 08-Sep-26 | 21-Sep-26 |
| 7 | MAGIC:OoB VH & Supp: Shipping period for the component | 1 | 15d | 0% | 22-Sep-26 | 12-Oct-26 |
| 8 | MAGIC:OoB VH & Supp: Component delivered to ESS | 1 | 0d | 0% | 13-Oct-26 | |
| 9 | MAGIC:OoB Guid+ VH & Supp: Physical integration of guide elements and housing at site | 1 | 10d | 0% | 13-Oct-26 | 26-Oct-26 |
| 10 | MAGIC:OoB Guid+ VH & Supp: Installation of the Guide system ( incl VH and supports) | 1 | 10d | 0% | 27-Oct-26 | 09-Nov-26 |
| 11 | MAGIC:OoB Guid+ VH & Supp: Preparation for SAT / TRR (prep period+ sign off) | 1 | 4d | 0% | 10-Nov-26 | 13-Nov-26 |
| 12 | MAGIC: All Out-Bunker SAT | 1 | 0d | 0% | | 25-Nov-26 |
| 13 | MAGIC:OoB Guid+ VH & Supp: Integrated SAT | 1 | 8d | 0% | 16-Nov-26 | 25-Nov-26 |
| 14 | MAGIC: Integrated cold commissioning | 1 | 20d | 0% | 26-Nov-26 | 23-Dec-26 |
| 15 | MAGIC: Instrument complete (TG5/SAR start) | 1 | 0d | 0% | | 23-Dec-26 |
| 16 | MAGIC: Preparation for TG5 review meeting (Float 2 months) | 1 | 40d | 0% | 07-Jan-27 | 03-Mar-27 |
| 17 | MAGIC: TG5/SAR meeting | 1 | 0d | 0% | | 03-Mar-27 |
| 18 | MAGIC: TG5/SAR action closeouts and approval | 1 | 40d | 0% | 04-Mar-27 | 28-Apr-27 |
| 19 | MAGIC TG5/SAR approval | 1 | 0d | 0% | | 28-Apr-27 |
| 20 | **MAGIC-2** | 21 | 203d | | 07-Jan-26 | 23-Nov-26 |
| 21 | MAGIC: Osc: Detailed design phase for the oscillation | 1 | 35d | 0% | 07-Jan-26* | 24-Feb-26 |
| 22 | MAGIC: Osc: Submission of docs to ESS for CDR/TG3 | 1 | 10d | 0% | 25-Feb-26 | 10-Mar-26 |
| 23 | MAGIC: Osc: Review of CDR documents by ESS | 1 | 10d | 0% | 11-Mar-26 | 24-Mar-26 |
| 24 | MAGIC: Osc: CDR (meeting) | 1 | 0d | 0% | 25-Mar-26 | |
| 25 | MAGIC: Osc: CDR: Closure of open points and approval | 1 | 10d | 0% | 25-Mar-26 | 09-Apr-26 |
| 26 | MAGIC: Osc: Procurement and manufacturing of the Oscillation | 1 | 60d | 0% | 10-Apr-26 | 08-Jul-26 |
| 27 | MAGIC: Osc: Factory Acceptance Test (FAT) | 1 | 0d | 0% | 09-Jul-26 | |
| 28 | MAGIC: Osc: FAT Report and Documentation | 1 | 5d | 0% | 09-Jul-26 | 15-Jul-26 |
| 29 | MAGIC: Osc: FAT-closure of open points and approval | 1 | 10d | 0% | 09-Jul-26 | 22-Jul-26 |
| 30 | MAGIC:RC+ Oscillation: Qgate document submission phase | 1 | 15d | 0% | 09-Jul-26 | 29-Jul-26 |
| 31 | MAGIC:RC+ Oscillation: Quality gate review and approval | 1 | 20d | 0% | 17-Aug-26 | 11-Sep-26 |
| 32 | MAGIC:RC+ Oscillation: IRR meeting preparation | 1 | 5d | 0% | 14-Sep-26 | 18-Sep-26 |
| 33 | MAGIC:RC+ Oscillation: TG4 passed | 1 | 0d | 0% | | 21-Sep-26 |
| 34 | MAGIC:RC+ Oscillation: Installation preparation | 1 | 3d | 0% | 21-Sep-26 | 23-Sep-26 |
| 35 | MAGIC:RC+ Oscillation: Installation of the Component | 1 | 5d | 0% | 24-Sep-26 | 30-Sep-26 |
| 36 | MAGIC:MCA Final energization of cabinets ( radial collimator) | 1 | 10d | 0% | 01-Oct-26 | 14-Oct-26 |
| 37 | MAGIC:MCA: Setting up of control systems (Radial collima) | 1 | 5d | 0% | 15-Oct-26 | 21-Oct-26 |
| 38 | MAGIC:MCA: Commissioning of subsystem related to respective cabinets (radial collim) | 1 | 10d | 0% | 22-Oct-26 | 04-Nov-26 |
| 39 | MAGIC:MCA: Configuration of interfaces to EPICS/NICOS (radial collim) | 1 | 5d | 0% | 05-Nov-26 | 11-Nov-26 |
| 40 | MAGIC:RC+ Oscillation: Integrated SAT | 1 | 8d | 0% | 12-Nov-26 | 23-Nov-26 |
| 41 | MAGIC:MCA: Local SAT Inst zone (including EPICS/NICOS) (radial collim) | 1 | 8d | 0% | 12-Nov-26 | 23-Nov-26 |
| 42 | **MAGIC-3** | 19 | 395d | | 12-Feb-25 A | 13-Nov-26 |
| 43 | MAGIC: Supp-Analtr+Det B: Detailed design phase for the Supports | 1 | 206d | 76.7% | 12-Feb-25 A | 05-Dec-25 |
| 44 | MAGIC: Supp-Analtr+Det B: Submission of docs to ESS for CDR/TG3 | 1 | 10d | 0% | 08-Dec-25 | 19-Dec-25 |
| 45 | MAGIC: Supp-Analtr+Det B: Review of CDR documents by ESS | 1 | 10d | 0% | 22-Dec-25 | 16-Jan-26 |
| 46 | MAGIC: Supp-Analtr+Det B: CDR (meeting) | 1 | 0d | 0% | 19-Jan-26 | |
| 47 | MAGIC: Supp-Analtr+Det B: CDR: Closure of open points and approval | 1 | 10d | 0% | 19-Jan-26 | 30-Jan-26 |
| 48 | MAGIC: Supp-Analtr+Det B: Procurement and manufacturing of the Component | 1 | 100d | 0% | 02-Feb-26 | 29-Jun-26 |
| 49 | MAGIC: Supp-Analtr+Det B: Factory Acceptance Test (FAT) | 1 | 0d | 0% | 30-Jun-26 | |
| 50 | MAGIC: Supp-Analtr+Det B: FAT Report and Documentation | 1 | 5d | 0% | 30-Jun-26 | 06-Jul-26 |
| 51 | MAGIC: Supp-Analtr+Det B: FAT-closure of open points and approval | 1 | 10d | 0% | 30-Jun-26 | 13-Jul-26 |
| 52 | MAGIC: Supp-Analtr+Det B: Qgate document submission phase | 1 | 15d | 0% | 30-Jun-26 | 20-Jul-26 |
| 53 | MAGIC: Supp-Analtr+Det B: Quality gate review and approval | 1 | 20d | 0% | 17-Aug-26 | 11-Sep-26 |
| 54 | MAGIC: Supp-Analtr+Det B: IRR meeting preparation | 1 | 5d | 0% | 14-Sep-26 | 18-Sep-26 |
| 55 | MAGIC: Supp-Analtr+Det B: Installation readiness review (IRR) | 1 | 0d | 0% | 21-Sep-26 | |
| 56 | MAGIC: Supp-Analtr+Det B: TG4 passed | 1 | 0d | 0% | | 21-Sep-26 |
| 57 | MAGIC: Supp-Analtr+Det B: Installation preparation | 1 | 5d | 0% | 21-Sep-26 | 25-Sep-26 |
| 58 | MAGIC: Supp-Analtr+Det B: Installation of the Component | 1 | 5d | 0% | 28-Sep-26 | 02-Oct-26 |
| 59 | MAGIC: Analyzer Seg 1: Installation of the Component | 1 | 11d | 0% | 05-Oct-26 | 19-Oct-26 |
| 60 | MAGIC: Analyzer Seg 1: Preparation for SAT / TRR (prep period+ sign off) | 1 | 6d | 0% | 20-Oct-26 | 27-Oct-26 |
| 61 | MAGIC: Analyzer Seg 1: Integrated SAT | 1 | 13d | 0% | 28-Oct-26 | 13-Nov-26 |
| 62 | **MAGIC-4** | 18 | 286d | | 18-Aug-25 A | 10-Nov-26 |
| 63 | MAGIC:Supp-RC+Det A: Detailed design phase for the Supports | 1 | 84d | 38.1% | 18-Aug-25 A | 11-Dec-25 |
| 64 | MAGIC:Supp-RC+Det A: Submission of docs to ESS for CDR/TG3 | 1 | 10d | 0% | 12-Dec-25 | 08-Jan-26 |
| 65 | MAGIC:Supp-RC+Det A: Review of CDR documents by ESS | 1 | 10d | 0% | 09-Jan-26 | 22-Jan-26 |
| 66 | MAGIC:Supp-RC+Det A: CDR (meeting) | 1 | 0d | 0% | 23-Jan-26 | |
| 67 | MAGIC:Supp-RC+Det A: CDR: Closure of open points and approval | 1 | 10d | 0% | 23-Jan-26 | 05-Feb-26 |
| 68 | MAGIC:Supp-RC+Det A: Procurement and manufacturing of the Component | 1 | 100d | 0% | 06-Feb-26 | 03-Jul-26 |
| 69 | MAGIC:Supp-RC+Det A: Factory Acceptance Test (FAT) | 1 | 0d | 0% | 06-Jul-26 | |
| 70 | MAGIC:Supp-RC+Det A: FAT Report and Documentation | 1 | 5d | 0% | 06-Jul-26 | 10-Jul-26 |
| 71 | MAGIC:Supp-RC+Det A: FAT-closure of open points and approval | 1 | 10d | 0% | 06-Jul-26 | 17-Jul-26 |
| 72 | MAGIC:Supp-RC+Det A: Qgate document submission phase | 1 | 15d | 0% | 06-Jul-26 | 24-Jul-26 |
| 73 | MAGIC:Supp-RC+Det A: Quality gate review and approval | 1 | 15d | 0% | 17-Aug-26 | 04-Sep-26 |
| 74 | MAGIC:Supp-RC+Det A: Installation readiness review (IRR) | 1 | 0d | 0% | 07-Sep-26 | |
| 75 | MAGIC:Supp-RC+Det A: TG4 passed | 1 | 0d | 0% | | 07-Sep-26 |
| 76 | MAGIC:Supp-RC+Det A: Installation preparation | 1 | 5d | 0% | 07-Sep-26 | 11-Sep-26 |
| 77 | MAGIC:Supp-RC+Det A: Installation of the Component | 1 | 5d | 0% | 14-Sep-26 | 18-Sep-26 |
| 78 | MAGIC: Det A: Installation of the Component | 1 | 10d | 0% | 01-Oct-26 | 14-Oct-26 |
| 79 | MAGIC: Det A: Preparation for SAT / TRR (prep period+ sign off) | 1 | 4d | 0% | 15-Oct-26 | 20-Oct-26 |
| 80 | MAGIC: Det A: Integrated SAT | 1 | 15d | 0% | 21-Oct-26 | 10-Nov-26 |
| 81 | **MAGIC-5** | 22 | 371d | | 04-Mar-25 A | 30-Oct-26 |
| 82 | MAGIC: Sample St: Detailed design phase for the Sample Station | 1 | 188d | 63.83% | 04-Mar-25 A | 16-Jan-26 |
| 83 | MAGIC: Sample St: Submission of docs to ESS for CDR/TG3 | 1 | 15d | 0% | 19-Jan-26 | 06-Feb-26 |
| 84 | MAGIC: Sample St: Review of CDR documents by ESS | 1 | 10d | 0% | 09-Feb-26 | 20-Feb-26 |
| 85 | MAGIC: Sample St: CDR (meeting) | 1 | 0d | 0% | 23-Feb-26 | |
| 86 | MAGIC: Sample St: CDR: Closure of open points and approval | 1 | 10d | 0% | 23-Feb-26 | 06-Mar-26 |
| 87 | MAGIC: Sample St: Procurement and manufacturing of the Component | 1 | 46d | 0% | 09-Mar-26 | 18-May-26 |
| 88 | MAGIC: Sample St: Factory Acceptance Test (FAT) | 1 | 0d | 0% | 19-May-26 | |
| 89 | MAGIC: Sample St: FAT Report and Documentation | 1 | 5d | 0% | 19-May-26 | 25-May-26 |
| 90 | MAGIC: Sample St: FAT-closure of open points and approval | 1 | 5d | 0% | 19-May-26 | 25-May-26 |
| 91 | MAGIC: Sample St: Qgate document submission phase | 1 | 15d | 0% | 08-May-26 | 01-Jun-26 |
| 92 | MAGIC: Sample St: Quality gate review and approval | 1 | 15d | 0% | 02-Jun-26 | 23-Jun-26 |
| 93 | MAGIC: Sample St: IRR meeting preparation | 1 | 5d | 0% | 24-Jun-26 | 30-Jun-26 |
| 94 | MAGIC: Sample St: Installation readiness review (IRR) | 1 | 0d | 0% | 01-Jul-26 | |
| 95 | MAGIC: Sample St: TG4 passed | 1 | 0d | 0% | | 01-Jul-26 |
| 96 | MAGIC: Sample St: Installation preparation | 1 | 5d | 0% | 01-Jul-26 | 07-Jul-26 |
| 97 | MAGIC: Sample St: Installation of the Component | 1 | 5d | 0% | 08-Jul-26 | 14-Jul-26 |
| 98 | MAGIC:MCA Final energization of cabinets ( slits,sample stage) | 1 | 10d | 0% | 15-Jul-26 | 25-Aug-26 |
| 99 | MAGIC:MCA: Setting up of control systems | 1 | 10d | 0% | 26-Aug-26 | 08-Sep-26 |
| 100 | MAGIC:MCA: Commissioning of subsystem related to respective cabinets | 1 | 15d | 0% | 09-Sep-26 | 29-Sep-26 |
| 101 | MAGIC:MCA: Configuration of interfaces to EPICS/NICOS | 1 | 10d | 0% | 30-Sep-26 | 13-Oct-26 |
| 102 | MAGIC: Sample St: Integrated SAT | 1 | 8d | 0% | 21-Oct-26 | 30-Oct-26 |
| 103 | MAGIC:MCA: Local SAT Inst zone (including EPICS/NICOS) | 1 | 13d | 0% | 14-Oct-26 | 30-Oct-26 |

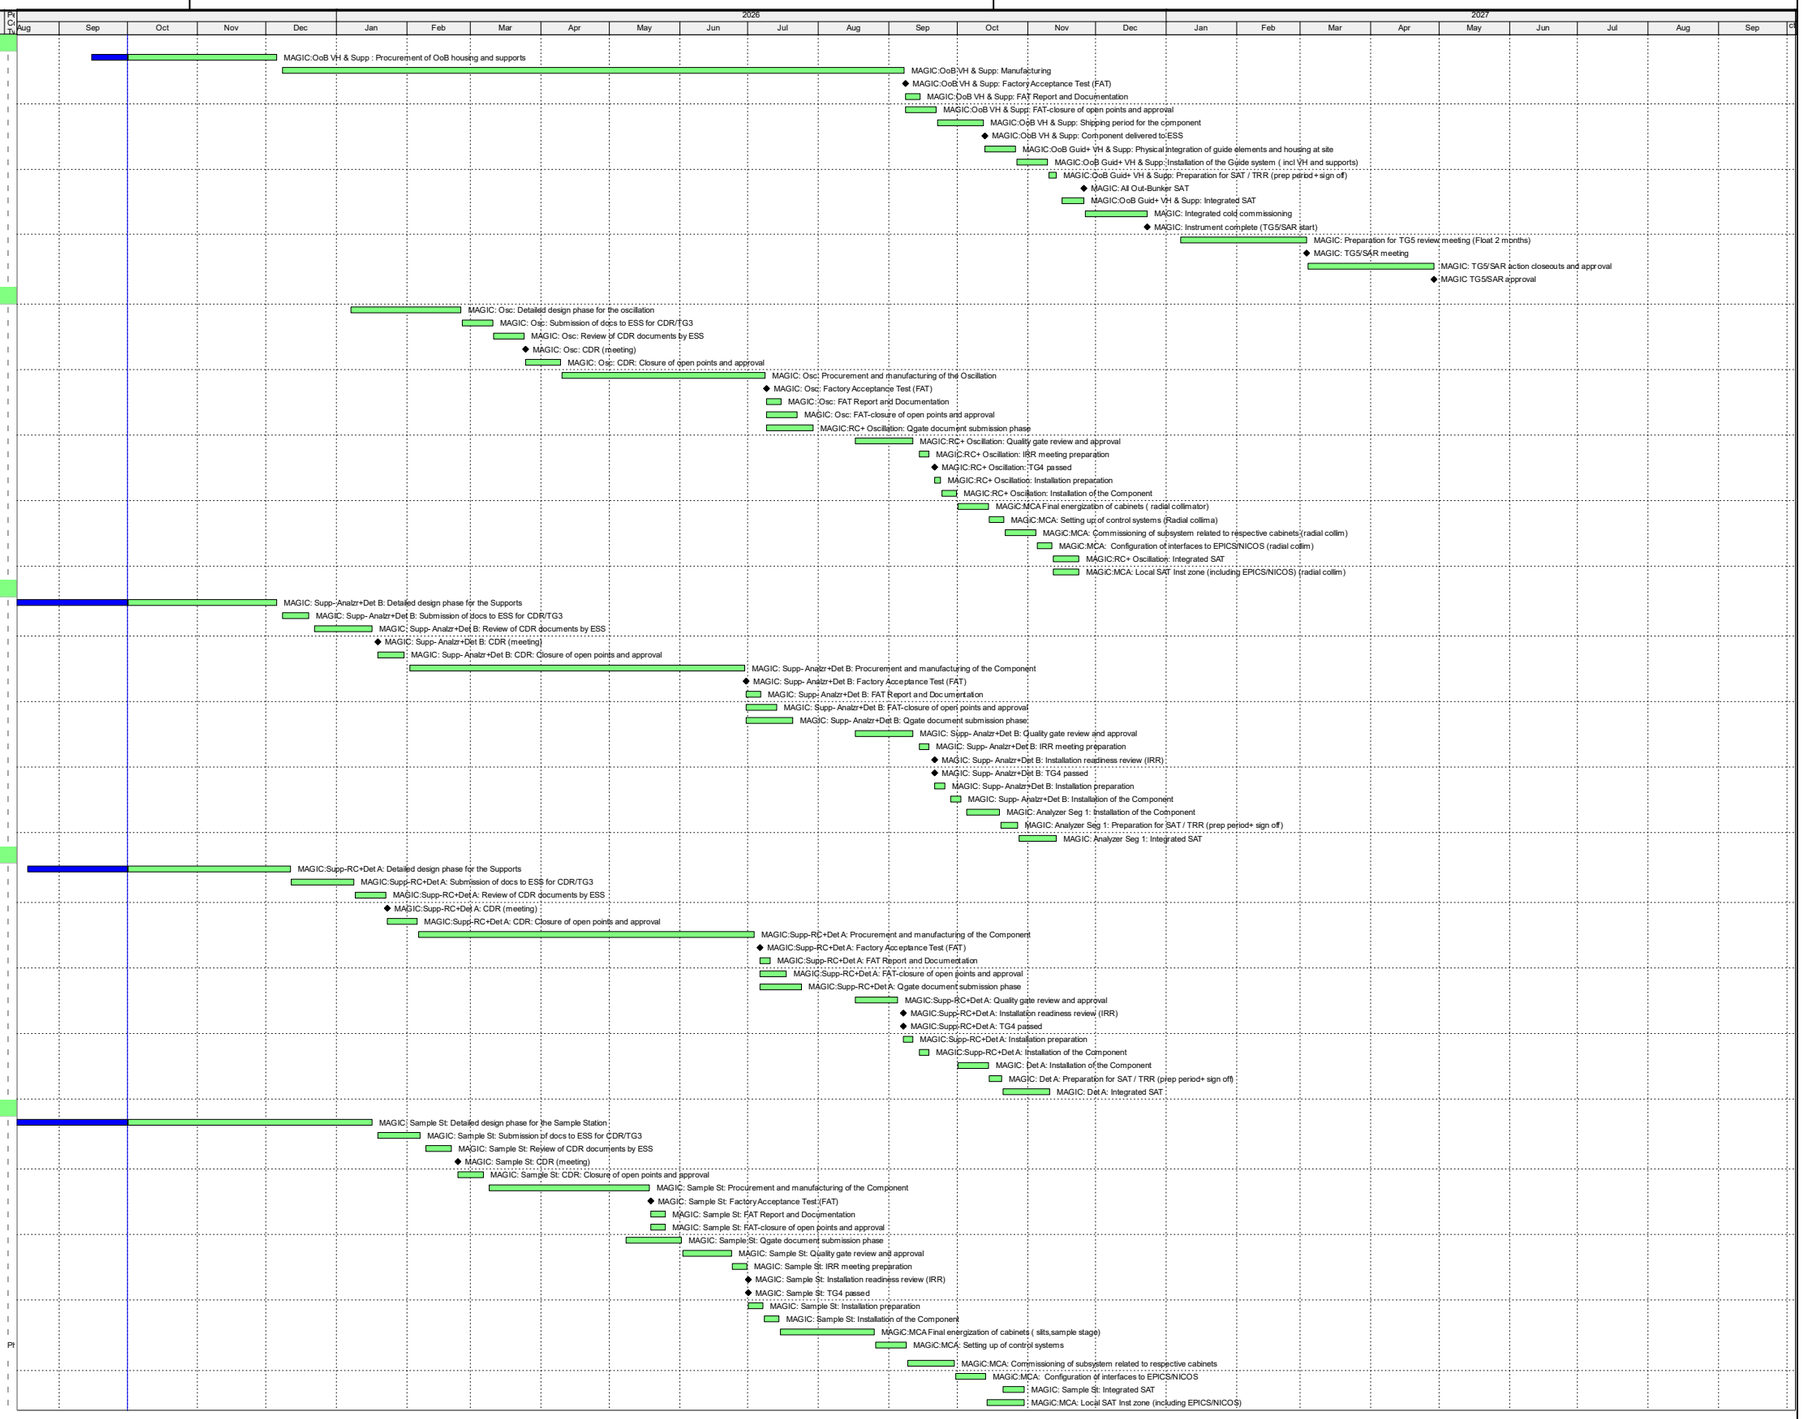


Remaining Level of Effort | Actual Work | Critical Remaining ...
Actual Level of Effort | Remaining Work | Milestone



TASK filters: (Untitled Filter), Start greater than Dec 31 2021.

© Oracle Corporation
